



**AUSTRALIAN
ACCESS FEDERATION**

www.aaf.edu.au

PROGRESS REPORT 4

30 JUNE 2011

.....

This document is the fourth Australian Access Federation Project Progress Report for the period of 1 January 2011 to 30 June 2011.

.....

Project Title: Australian Access Federation

Report Period: 1 January 2011 – 30 June 2011





19 July 2011

Clare McLaughlin
General Manager
Research Infrastructure Branch
Science and Infrastructure Division
Department of Innovation, Industry, Science and Research
GPO Box 9839,
Canberra ACT 2601

Dear Clare,

This report constitutes the fourth Progress Report for the Australian Access Federation Implementation Project, as per the revised reporting schedule (for 31 December 2011 extension) and required under Schedule 3 of the Funding Agreement. The report relates to the period of 1 January 2011 to 30 June 2011 and highlights the continuing progress of the Australian Access Federation Project in achieving its objectives and milestones. To date the implementation of the Australian Access Federation has been a tremendously collaborative and successful endeavour and the activities of the project continue to be governed by the AAF Inc Executive Committee.

Please contact me with any queries relating to the Progress Report or for further details of the project's activities.

Yours sincerely



Paul Sherlock
President, Australian Access Federation (AAF) Inc.

Cc: Ms Kate Hurford

PROGRESS REPORT 4 30 JUNE 2011

CONTENTS

1. Introduction	4
1.1 Name of Recipient and all Subcontractors	4
1.1.1 Name of all Subcontractors.....	4
1.2 Project Details.....	5
1.3 Statement of Funds, Recipient Contributions and Other Contributions received and spent	5
1.4 Amount Remaining in the Account	5
2. Description and Analysis of the Progress of the Australian Access Federation Project	6
2.1 Milestones Achieved	6
2.2 Project Budget.....	14
2.3 Progress on Achieving Outcomes	14
2.4 Major Issues or Developments and their effect on the project.....	14
2.5 Proposed Changes to the Project.....	14
3. Activities, Published Reports, Promotional Material, Media Publicity, Pamphlets or Other Documentation.....	15
Project Contacts	17
APPENDIX A: Statement of Funds, Recipient Contributions and other Contributions received and spent for the period (Income Statement I January 2011 to 30 June 2011)	18
APPENDIX B: 30 June 2011 Annual General Meeting Agenda	19
APPENDIX C: AAF Promotional Material	20

I. INTRODUCTION

The Australian Access Federation (AAF) project is continuing to progress well, in-line with the project schedule and budget.

This report relates to the period 1 January 2011 to 30 June 2011. Key highlights of the AAF Implementation Project over the reporting period have been:

- the collection of 2011 subscription fees;
- the completion of a number of the AAF Mini-grants;
- the election of a new AAF Inc Executive Committee (at the 30 June 2011 AGM);
- preparation of the 2010 Annual Report; and
- progress towards a number of activities outlined in the 2011 AAF Inc Business Plan.

1.1 Name of Recipient and all Subcontractors

Queensland University of Technology on behalf of the Council of Australian University Directors of Information Technology (CAUDIT).

1.1.1 Name of all Subcontractors

To date the AAF has engaged with a number of subcontractors for the provision of services and subcontracts have also been established for the recipients of the AAF enabled Services Mini-grant Scheme. Table 1 shows details of completed subcontracts whilst Table 2 shows details of current subcontracts.

Subcontractor	Description	Subcontract period
Macquarie University	AAF MAMSTestbed Transition	01/07/2009 – 07/04/2010
The University of Queensland	AAF Policy, Strategy and Process Development Specialist	01/10/2009 – 31/03/2010
Australian Research Collaboration Services	AAF Policy, Strategy and Process Development Specialist	1/04/2010-30/06/2011
Griffith University	AAF Change and Communication Manager	14/09/2009 -17/09/2010
Griffith University	AAF Project Manager	20/07/2009-21/01/2011
Melbourne University (VeRS)	Technical Support	1/03/2010 - 31/12/2010
CSIRO	AAF Enabled Services Round 1 Mini-grant recipient	Completed on 30 April 2010
Monash University	AAF Enabled Services Round 2 Mini-grant recipient	1/02/2010 – 30/06/2010 (Extended till: 28/02/11)
RMIT Publishing	AAF Enabled Services Round 2 Mini-grant recipient	1/03/2010 – 25/08/2010
University of Tasmania	AAF Enabled Services Round 2 Mini-grant recipient	1/07/2010 – 31/12/2010
Australian Research Collaboration Service	AAF Enabled Services Round 3 Mini-grant recipient	1/09/10 – 1/11/2010
University of Technology Sydney	AAF Enabled Services Round 3 Mini-grant recipient	13/09/2010 – 13/04/2011 (Extended till: 31/03/11)

Table 1: AAF Implementation Project Subcontractors (Completed)

Subcontractor	Description	Subcontract period
Griffith University	AAF Change and Communication Manager	20/09/2010 – 1/07/2011
Intersect Australia	Technical Support	1/04/2010 - 31/12/2010 (Extended till: 31/10/2011)
The University of Queensland	AAF Enabled Services Round 2 Mini-grant recipient	1/07/2010 – 31/12/2010 (Extended till: 31/08/2011)
University of South Australia	AAF Enabled Services Round 2 Mini-grant recipient	15/02/2010 – 15/05/2010 (Extended till: 18/03/11)
Flinders University	AAF Enabled Services Round 3 Mini-grant recipient	1/08/2010 – 31/12/2010 New Subcontract entered into: 1/01/2011 - 26/08/11
The University of Queensland	AAF Enabled Services Round 3 Mini-grant recipient	1/07/2010 – 31/12/2010 (Extended till: 12/08/2011)
University of Southern Queensland	AAF Enabled Services Round 3 Mini-grant recipient	1/11/2010 – 31/03/2011 (Extension in train)

Table 2: AAF Implementation Project Subcontractors (Current)

1.2 Project Details

The details of the project are:

Project Title: Australian Access Federation Project

Reporting Period: 1 January 2011 to 30 June 2011

1.3 Statement of Funds, Recipient Contributions and Other Contributions received and spent

The Statement of Funds, Recipient Contributions and other Contributions received and spent for the period 1 January 2011 to 30 June 2011 is outlined in Appendix A.

1.4 Amount Remaining in the Account

As of 30 June 2011 the *Closing Retained Funds* was \$474,151.07 (see Appendix A).

2. DESCRIPTION AND ANALYSIS OF THE PROGRESS OF THE AUSTRALIAN ACCESS FEDERATION PROJECT

2.1 Milestones Achieved

A number of project milestones have been achieved during the reporting period. An update on their progress is discussed in this section.

Milestone 1: AAF Inc Registered as an Incorporated Association

Due Date: July 2009

Status: Complete (completion date: 23 June 2009).

The activities in achieving this milestone were reported in Progress Report 1.

Milestone 2: *Appointment/Secondment of an AAF Project Manager*

Due Date: August-September 2009

Status: Complete (completion date: 14 July 2009).

The activities in achieving this milestone were reported in Progress Report 1.

The project staffing as at 30 June 2011 was:

- AAF Manager (AAF Inc)
- Technical Manager (QUT)
- AAF Communications (Griffith University)
- Technical Architect (QUT)
- Technical Support Specialist (Intersect)
- Policy, Process, Strategy (ARCS)

Milestone 3: *Inaugural Meeting of the AAF Inc Interim Executive Committee*

Due Date: August 2009

Status: Complete (completion date: 25 August 2009).

The activities in achieving this milestone were reported in Progress Report 1.

Milestone 4: *Tender for AAF Operator Issued*

Due Date: September – October 2009

Status: Tender process terminated on 30 June 2010

The activities associated with the termination of this milestone were reported in Progress Report 3:

Milestone 5: *Call for Mini-grant Proposals Round 1*

Due Date: October - November 2009

Status: Complete. Round 1 of the Mini-grant scheme opened on 1/10/2009.

The activities in achieving this milestone were reported in Progress Report 1, 2 and 3.

At the end of the reporting period the Monash University, Tasmanian Partnership of Advanced Computing, University of Technology Sydney and the ARCS Mini-grants have completed. As advised in the Progress Report 3, many of the grants experienced delay in commencing activities because of the time taken to negotiate the subcontract agreements (this has been largely outside the control of the AAF Project). A number of the grants have since had their Subcontract Term extended and it is expected that they will complete in the next reporting period.

As part of the grant requirements, the recipient is required to submit a monthly progress report. The AAF project continues to monitor all grant activities and provide technical support as necessary. Table 3 provides a summary of the status of each mini-grant as of 30 June 2011.

Despite the scheme closing, the project has still continued to receive further requests for funding, representing the high demand for grants to assist with AAF enabling applications.

Recipient	Grant Activity	Amount	Status
Round 1			
CSIRO	AuScope Grid Portal Infrastructure	\$37,000	Complete
Round 2			
Monash University	ARCS' Nimrod Service	\$40,000	Complete
Queensland University of Technology	Advanced Shibboleth Integration with Blackboard	\$39,600	In train
RMIT Publishing	Informit	\$36,000	Complete
Tasmanian Partnership of Advanced Computing	TPAC Portal	\$40,000	Complete
University of Queensland	PODD	\$35,271	In train
University of South Australia	University IT Benchmarking System	\$20,000	In train
Round 3			
Flinders University	AusStage	\$40,000	In train
University of Queensland	Authenticated Annotation Services for E-Research (AASER)	\$39,700	In train
University of Southern Queensland and Automated Patrol Telescopes Australia	Connect <i>telescope-net</i> to the AAF	\$37,500	In train
University of Technology Sydney	Labshare Federated Access Project	\$30,000	Complete
Australian Research Collaboration Services	Sakai	\$9,600	Complete

Table 3: AAF Mini-grant Status as of 30/06/2011

Milestone 6: *Transition of the MAMS Testbed Participants to the AAF*

Due Date: November-December 2009

Status: Complete (14/12/2009).

The activities in achieving this milestone were reported in Progress Report 1.

Milestone 7: *The AAF Operator Appointed and Contract Signed*

Due Date: January – March 2010

Status: Operator RFO process terminated on 30 June 2010 (refer Milestone 4)

Milestone 8: *AAF Accelerated Technical Development Finalised*

Due Date: January – March 2010

Status: Complete.

The AAF completed its accelerated technical development activity in 2010 with the release of the 'Federation Registry' (to assist with the technical managing of Identity Providers and services in the Federation). During the reporting period the AAF further enhanced this application with the addition of a reporting module. The reporting module will be released in August 2011 and will provide a graphical representation of the activities of the Federation's utilisation as well as specific utilisation reports based on role (e.g. AAF only reports vs reports that only a Subscriber can see). The module is fully integrated with the Federation Registry tool.

Since the release of the Federation Registry tool, a number of international Federations have expressed interest in using the tool to manage their Federation (the code base for the Federation Registry was released to the international community via the Apache License Version 2.0, for open source projects in late 2010).

During the reporting period the AAF has also developed an operational technical roadmap. The roadmap's purpose is to assist the AAF keep abreast of the ongoing technical activities it needs to undertake to continue to provide a solid, robust and technically advanced Federation.

Milestone 9: AAF Support Team Fully Operational and Assisting Members

Due Date: February 2010

Status: Complete - Support team operational February 2010 and related activities are in train.

Over the reporting period the 2011 support strategy became fully operational and the AAF staff continued to provide a high level of support to all AAF Subscribers.

As outlined in the 2011 Business Plan, support to assist AAF Subscribers has focused on a number of key areas (listed below).

Support for New Subscribers (Subscriber Expansion): AAF personnel have continued to support remaining Australian Universities to join the AAF during 2011. In particular the AAF has continued to provide:

1. Policy advice on the Federation Rules; and
2. Technical advice to connect as an Identity and or Service provider to the Federation.

Service Expansion: The AAF has continued to identify and target organisations that provide support services and applications of value to the sector.

Product Marketing & Communications: The success of the AAF is measured in terms of adoption of federated access by the Research and Education community. The AAF team has continued to market and promote its products.

Milestone 10: AAF Production System with AAF Operator Goes Live

Due Date: February – April 2010

Status: Operator RFO process terminated on 30 June 2010 (refer Milestone 4).

The AAF has been operating a Production Federation since June 2009 (see Milestone 12).

Milestone 11: Mini-grant Proposal Round 1 Awarded

Due Date: April-March 2010

Status: Complete.

The activities in achieving this milestone were reported in Progress Report 2.

Milestone 12: Transition from Pilot AAF to Production AAF Completed

Due Date: April-May 2010

Status: Complete.

The activities in achieving this milestone were reported in Progress Report 1 and 2.

Milestone 13: Intensive Marketing and Communication Program Launched

Due Date: March 2010

Status: Launched January 2010 and related activities are in train - ongoing.

The marketing and communication program continued over the reporting period. The project’s focus has been to implement communication strategies to assist with federation growth to achieve the required Subscriber levels for ongoing self-sustainability.

The AAF continued to execute a comprehensive marketing and communication plan over the reporting period. Activities included:

1. 2010 AAF Inc Annual Report;
2. AAF Newsletters;
3. case studies and the AAF website;
4. distribution of AAF merchandise;
5. promotion of AAF activities and services of value through the Mini-grant scheme; and
6. providing a content rich website and service catalogue.

Figure 2 shows actual subscribers versus estimated subscribers from 1 January 2010 to 30 December 2011. The number of estimated subscribers was used to set the subscription fees for 2011. The AAF admitted 8 new subscribers over the reporting period, however 3 subscribers decided not to renew their subscription in 2011. There were 63 Subscribers in total as of 30 June 2011.

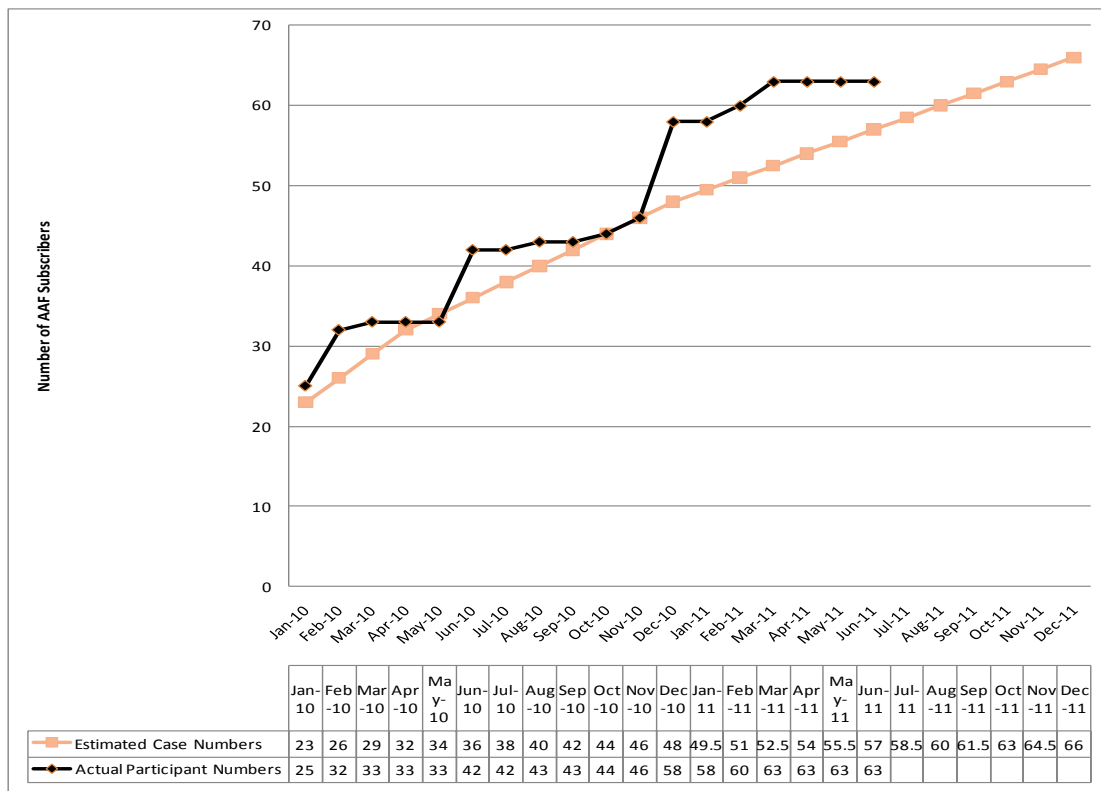


Figure 2: AAF Subscribers (1 January 2010 – 31 December 2011)

Although website visits were slightly down over the last reporting period, the AAF website has continued to receive strong visitor access (5,231 visitors from 75 countries accessed the website),

demonstrating continued interest in the AAF's activities. See Table 4 for the top 10 visitors by country.

Rank	Country	Visits
1	Australia	4,304
2	New Zealand	276
3	United States	106
4	United Kingdom	86
5	Canada	61
6	Netherlands	29
7	Brazil	27
8	Spain	23
9	India	21
10	Japan	20

Table 4: Top 10 AAF website visitors - 1 January 2011 to 30 June 2011

Section 3 of this Report discusses the published reports, promotional material, media publicity and pamphlets produced by the project as part of the Marketing and Communication Plan.

Milestone 14: *First Annual General meeting of the AAF*

Due Date: October 2010

Status: Complete (15 October 2010).

AAF Inc held its second Annual General Meeting on 30 June 2011 (see Appendix B for the Agenda). The AAF Executive Committee was re-elected at the meeting (see Table 5 for the elected office bearers).

Position	Name	Institution
President	Mr Paul Sherlock	University of South Australia
Vice President	Mr David Toll	CSIRO
Treasurer	Mr Marc Bailey	Macquarie University
Secretary	Mr Bruce Callow	Griffith University
Public Officer	Mr Richard Northam	CAUDIT Inc.
Member at Large	Mr Garry Trinder	Edith Cowan University
Member at Large	Mr John Parry	University of Tasmania

Table 5 AAF Inc Executive Committee - 30 June 2011

Over the reporting period Executive Committee Meetings were held on 7 February, 16 March and 24 May 2011.

Milestone 14: *On the completion of the project in December 2011, the AAF Membership and AAF enabled services should reach a critical mass for sustainability*

Due Date: December 2011

Status: In train.

As part of the submission of the second DIISR Progress report (30 June 2010), a request was made to extend the project by 1 year (to 31 December 2011). The Business Plan and subscription model was predicated on this happening. DIISR approved this request based on the addition of this new milestone.

Commencement of Levying AAF Subscription Fees for Sustainability

On 1 January 2011 the AAF commenced levying a Subscription fee on all organisations using AAF services. As of 30 June 2011 the AAF had received 98% of the subscription fees that it had invoiced.

New Subscriptions over the Reporting Period

Over the reporting period 8 new institutions and organisations subscribed to the AAF. As of 30 June 2011 95% of Australian Universities had subscribed to the Federation. The remaining two Australian Universities have signalled their intention to subscribe in the latter half of 2011. A full list of AAF subscribers can be found at <http://www.aaf.edu.au/subscribe/subscribers/>.

Activities as per the Australian Access Federation Inc. 2011 Business Plan

The four strategic phases of operation (as per the AAF Inc Business Plan) are represented in Figure 3 (below).

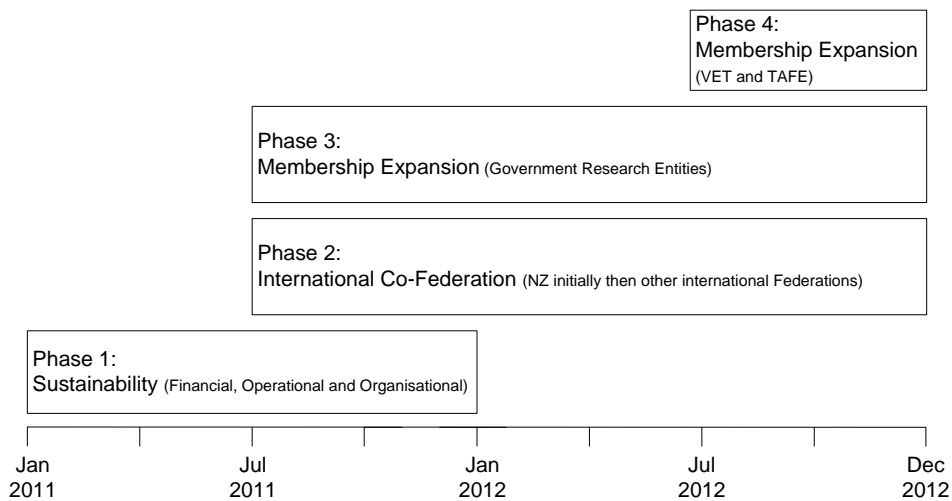


Figure 3: 2011 – 2012 Strategic Phases

Phase I of the strategy has commenced and a number of business activities are in train to assist the AAF with achieving a critical mass for sustainability:

1. **Financial Sustainability** through achieving Participant growth.
The AAF has continued supporting new Subscribers by providing policy advice and technical advice and identifying and targeting organisations that provide support services and applications of value to the sector. The AAF has also continued its product marketing efforts that focus on promoting the AAF's value proposition.

2. **Operational Sustainability**
Over the reporting period operational sustainability activities have included: providing *ongoing support services* to existing Subscribers to gain value from being part of the AAF and the development and launch of the 'annual compliance' strategy for compliance to the Federation Rules. All Subscribers are required to submit their first compliance statement on or before 30 June 2011.

The AAF has also continued (where possible) to maintain its current operational support model for personnel, core infrastructure and cloud based services.

3. **Organisational Sustainability**
As the AAF is a CAUDIT sponsored activity the AAF has continued to look for opportunities to rationalise its administration and governance activities between AAF Inc and CAUDIT Inc to keep operating costs and Member subscriptions of both organisations to a minimum. Activities to date have included CAUDIT Inc providing management activities for AAF Inc's financial affairs as well as supporting the AAF Inc's legislative and reporting requirements under the Associations Act of NSW.

2.2 Project Budget

The project is proceeding in accordance with the Budget. Table 6 outlines the expenditure to 30 June 2011 against the Budget in Schedule 4 of the Funding Agreement.

A budget variation request was approved by DIISR on 1 April 2011.

Activity Number	Activity Description	Revised Budget (1 April 2011)	Expenditure 1 January 2011 - 30 June 2011	Total Expenditure 1 July 2009 - 30 June 2011
2.1	MAMS Testbed migration	\$144,000	\$0	\$144,000
2.2	Technical resources to assist organizations to join the AAF	\$320,000	\$170,956	\$303,379
2.3	Marketing and communication	\$305,000	\$54,263	\$237,734
2.4	Mini-grant program	\$420,000	\$96,038	\$304,205
2.5	CAUDIT support	\$158,000	\$100,104	\$141,228
2.6	AAF Inc operations	\$374,000	\$23,267	\$236,959
2.7	Foundation members support	\$139,000	\$45,699	\$140,515
2.8	Advanced technical developments	\$140,000	\$0	\$140,560
Investment Income ¹	Interest earned on account	N/A	\$(17,263)	\$(122,733)
Total:		\$2,000,000	\$473,099	\$1,525,849

Table 6: Project Budget Expenditure to 30 June 2011

As at 30 June 2011 the *Closing Retained Funds* on the project account was \$474,151.07.

2.3 Progress on Achieving Outcomes

The AAF project is progressing well and in line with the project plan and budget.

2.4 Major Issues or Developments and their effect on the project

None

2.5 Proposed Changes to the Project

None

¹ Interest earned on the funds has been applied to the account (as per clause 9.4 of the Funding Agreement).

3. ACTIVITIES, PUBLISHED REPORTS, PROMOTIONAL MATERIAL, MEDIA PUBLICITY, PAMPHLETS OR OTHER DOCUMENTATION

A number of event activities occurred during the reporting period. These are outlined in Table 7.

Event	Date	Description
AAF Training Session	14-15 February 2011	Perth (on request from CSIRO a 2 day training session in Shibboleth and IdP configuration was run by the Technical Team)
AAF Services Authorisation Workshop (Perth)	16 February 2011	WA universities and CSIRO – a 1 day workshop focusing on how we authorise individuals and groups to access services and the tools to support policy decisions.
Research Infrastructure Roadmap Expert (RIRE) Working Group	24 February 2011	The AAF Manager presented to the RIRE Working Group which is developing a new Strategic Roadmap for Australian Research Infrastructure in 2011.
CCA-EDUCAUSE Australasia 2011	3-6 April 2011 March	The AAF presented 2 Lightning rounds and the Poster Event: Round 1: Innovative Federation Uses: Telescopes, Labs, and clouds Round 2: <i>The Future of Identity Federations – where will they add value?</i> Poster Event: <i>AAF - the game has changed for access to services.</i>
REFEDS Meeting	15 May 2011	The AAF Manager represented the AAF at the REFEDS meeting in Prague, Czech Republic
TERENA Networking Conference 2011	16-19 May 2011	The AAF Manager represented the AAF at TERENA in Prague, Czech Republic

Table 7: AAF Events

Table 8 outlines the communications and media that were generated during the reporting period.

Key Activity	Media and Communication
AAF Maintenance Window and reminder, FR upgrade, system outage (5 articles)	AAF website, Twitter, Facebook
Federated Registry toolset available to other federations	AAF website, Twitter, Facebook
AAF Growth	eResearch newsletter
Notice of AAF Services Workshop in Perth	eResearch newsletter
AAF Lightning Rounds at CCA-EDUCAUSE Australasia	AAF website, eResearch newsletter, Twitter, Facebook
CloudStor web service access	AAF website, Twitter, Facebook

through AAF (2 articles)	
Monash launches federated access to Nimrod Portal	AAF website
New look Service Catalogue	AAF website, Twitter, Facebook
AAF at REFEDS / TERENA (2 articles)	AAF website, Twitter, Facebook
Upgrade to TPAC Portal	eResearch newsletter
Notice of AAF AGM	AAF website, Twitter, Facebook
Compliance Statements (2 articles)	AAF website, Twitter, Facebook
Issue 3 of AAF Newsletter (June 2011)	Twitter, Facebook, Email listing from CRM, subscriber listing, CAUDIT membership (see Appendix C)

Table 8: AAF Communication and Media

The following promotional materials were produced by the project during the reporting period, as outlined in Table 9.

Key Activity	Description
Poster Event – CCA – EDUCAUSE Australasia 2011	AAF - the game has changed for access to services (see Appendix C)
AAF 2010 utilisation overview	Utilisation statistics (see Appendix C)

Table 9: AAF Promotional Materials

The following report was produced by the project during the reporting period, as outlined in Table 10.

Key Activity	Description
AAF 2010 Annual Report	The Annual Report covers the period 1 January to 31 December 2010 (see Appendix C)

Table 10: AAF Report

The following case study was produced by the project during the reporting period, as outlined in Table 11.

Key Activity	Description
Cloudstor	http://www.aaf.edu.au/wp-content/uploads/2010/03/CloudStor-Case-Study-Final.pdf

Table 11: AAF Case Studies

PROJECT CONTACTS

The project will be pleased to provide further information on the Australian Access Federation to DIISR officers. Key contact points are:

- **Mr Paul Sherlock**
President, Australian Access Federation Inc.
Director, Information Strategy and Technology Services
University of South Australia
Phone: 08 8302 3575
Email: Paul.Sherlock@unisa.edu.au
- **Mr Richard Northam**
Public Officer, Australian Access Federation Inc.
General Manager, CAUDIT
Phone: 02 6222 3521
Email: Richard.Northam@caudit.edu.au
- **Mr Heath Marks**
Manager, Australian Access Federation
Phone: 07 3138 1231
Email: Heath.Marks@aaf.edu.au

APPENDIX A: STATEMENT OF FUNDS, RECIPIENT
CONTRIBUTIONS AND OTHER CONTRIBUTIONS RECEIVED AND
SPENT FOR THE PERIOD (INCOME STATEMENT | JANUARY 2011
TO 30 JUNE 2011)

APPENDIX B: 30 JUNE 2011 ANNUAL GENERAL MEETING AGENDA



AUSTRALIAN ACCESS FEDERATION INC. ANNUAL GENERAL MEETING: 30 JUNE 2011

AGM AGENDA AND MEETING DETAILS:

Venue

Teleconference:




Australia 1800 766 715 (02 8524 6600) - Conference Code: 2858162108#
New Zealand 0800 445 473 – Conference Code: 2858162108#

DAY	DATE	QLD	NSW/ACT/Vic/TAS	SA	WA	NZ
Thursday	30 June	12:00 – 2:00 pm	12:00 – 2:00 pm	11:30 – 1:30 pm	10:00 – 12:00 pm	2:00 – 4:00 pm

AGENDA

1. **Welcome and Apologies** *Paul Sherlock (President)*
2. **Admittance of Proxies** *Paul Sherlock*
3. **Minutes of the Previous AGM (21 October 2010)** *Paul Sherlock*
Motion 1: Minutes
4. **President's Report** *Paul Sherlock*
5. **Reports** *Paul Sherlock*
 - a) DIISR Progress Report 3: 31 December 2010 (for information)
 - b) 2010 Annual Report (for information)
 - c) Audited Statement of Accounts
Motion 2: Audited Statement of Accounts
6. **Committee Elections** *Richard Northam (Public Officer)*
7. **Amendments to the AAF Inc Constitution - Membership of the Executive** *Paul Sherlock*
Motion 3: Amendments to AAF Inc Constitution - Membership of the Executive Committee
8. **Amendments to the AAF Inc Constitution - Term of Executive Committee Membership** *Paul Sherlock*
Motion 4: Amendments to AAF Inc Constitution - Term of Executive Committee Members
9. **Amendments to the AAF Inc Constitution - Amendment of wording to reference the Federation Rules** *Paul Sherlock*
Motion 5: Amendments to AAF Inc Constitution - Amendment of wording to reference the Federation Rules
10. **Amendments to the AAF Inc Constitution - Miscellaneous** *Paul Sherlock*
Motion 6: Amendments to AAF Inc Constitution - Miscellaneous

APPENDIX C: AAF PROMOTIONAL MATERIAL

Image	Document Title	Location
	<p>Issue 3 of AAF Newsletter (June 2011)</p>	<p>http://www.aaf.edu.au/about/news-events/australian-access-federation-newsletter-issue-3/</p>
	<p>AAF - the game has changed for access to services</p>	<p>Poster Event – CCA-EDUCAUSE Australasia 2011</p>
	<p>AAF 2010 utilisation overview</p>	<p>http://www.aaf.edu.au/wp-content/uploads/2009/09/2010-AAF-Flyer-v41.pdf</p>

	<p>AAF 2010 Annual Report</p>	<p>http://www.aaf.edu.au/wp-content/uploads/2009/09/FINAL-2010-AAF-ANNUAL-REPORT.pdf</p>
---	---------------------------------------	--
